



Town of
Midland



Wastewater Services Annual Report

2025

Definitions

The following defines terms that appear throughout this report and that will often be used for the duration of the report:

“BOD” – Biochemical Oxygen Demand

“Biosolids” - is a primarily organic solid product by wastewater treatment processes that can be beneficially recycled.

“CFU” - Colony-Forming Unit.

“Dissolved Oxygen” (DO) - the oxygen freely available in wastewater.

“ECA” - Environmental Certificate Approval.

“Final Effluent” - sewage discharge via the sewage treatment plant outfall after undergoing the full train of unit process.

“Geometric Mean Density” is the ninth root of the product of multiplication of the results of a number of the samples over the period specified.

“I&I” (Inflow and Infiltration) means dilution of sewage decreases the efficiency of treatment, and may cause sewage volumes to exceed design capacity.

“Limited Operational Flexibility” (LOF) means any modifications that the Owner is permitted to make to the works under this Approval.

“m³” - cubic meters.

“NASM” - Non-Agricultural Source Material.

“Overflow” means any discharge to the environment from the sewage Treatment Plant at a location other than the plant outfall (i.e.:storm equalization tank). This type of by-pass receives partial treatment before it is discharged to the environment.

“Owner” - The Corporation of the Town of Midland and its successors and assignees.

“Phosphorus” - a nonmetal of the nitrogen group.

“By-Pass” - diversion of sewage around one or more unit processes within the Sewage Treatment Plant with the diverted sewage flows being returned to the sewage Treatment Plant treatment train upstream of the final effluent sampling location and discharging to the environment through the sewage treatment plant outfall.

“PLC” - Programmable Logic Controller.

“SCADA” - Supervisory Control and Data Acquisition.

“Supernatant” - the relatively clear water layer between the sludge on the bottom and the scum on the surface of an anaerobic digester, septic tank or secondary clarifier.

“Total Ammonia” - the sum of both NH_3 and NH_4^+ .

“Water Supervisor” - the Water Supervisor for the Barrie Office of the Ministry.

A number of other technical terms have been used in this report but occur less frequently. Where necessary and to the reader’s benefit, definitions for these terms are provided as they occur.

Executive Summary

The purpose of the Town of Midland Wastewater Services Annual Report is to be a clear and concise assessment of the Wastewater Treatment and Collection system performance. Within the 2025 Reporting Year, there was **no failure to meet effluent limits and objectives**.

However, **two (2) overflows were reported**. For more information about the by-pass and overflows, refer to the *By-pass and Overflows* section on Page 20 of this report.

This report is to provide information to all applicable stakeholders and to satisfy the regulatory requirements of the **Amended Environmental Compliance Approval 5708-A72SPG** as issued July 20, 2016 and the **Consolidated Linear Infrastructure (CLI) for the Wastewater Collection System 122-W601** as issued August 15th, 2023.

The Town of Midland's Wastewater System was inspected April 26, 2023 by the local MECP Branch. The primary focus of this inspection was to confirm compliance with Ministry of the Environment legislation and control documents, as well as conformance with Ministry wastewater-related policies for the inspection period. The Ministry is implementing a rigorous and comprehensive approach in the inspection of wastewater treatment systems that focuses on the collection, treatment, and discharge components as well as wastewater treatment system management practices. **No issues of non-compliance or recommendations were noted in the report**. The inspection report is available upon request.

The Owner shall prepare and submit a performance report to the Director and Water Supervisor of the MECP on an annual basis, within ninety (90) days following the end of the period being reported upon. The first such report shall cover the first annual period following the commencement of operation of the works and subsequent reports shall be submitted to cover successive annual periods following thereafter. This report is also submitted to the District Manager where a Collection System Overflow or Spill of Sewage has occurred in the reporting period. The reports shall contain, but shall not be limited to, the following information.

Wastewater Treatment Reporting Requirements:

- a summary and interpretation of all monitoring data and a comparison to the effluent limits outlined in Condition 7, including an overview of the success and adequacy of the Works;
- a description of any operating problems encountered, and corrective actions taken;
- a summary of all maintenance carried out on any major structure, equipment, apparatus, mechanism or thing forming part of the Works;
- a summary of any effluent quality assurance or control measures undertaken in the reporting period;
- a summary of the calibration and maintenance carried out on all effluent monitoring equipment;

- a description of efforts made, and results achieved in meeting the Effluent Objectives of Condition 6.
- a tabulation of the volume of sludge generated in the reporting period, an outline of anticipated volumes to be generated in the next reporting period and a summary of the locations to where the sludge was disposed;
- a summary of any complaints received during the reporting period and any steps taken to address the complaints;
- a summary of all By-pass, spill or abnormal discharge events;
- a copy of all Notice of Modifications submitted to the Water Supervisor as a result of Schedule B, Section 1, with a status report on the implementation of each modification;
- a report summarizing all modifications completed as a result of Schedule B, Section 3; and;
- any other information the Water Supervisor requires from time to time.

Wastewater Collection System Report Requirements:

The Owner shall prepare an annual performance report for the Authorized System that:

- If applicable, includes a summary of all required monitoring data with an interpretation of the data and any conclusion drawn from the data evaluation about the need for future modifications to the Authorized System or system operations.
- Includes a summary of any operating problems encountered and corrective actions taken.
- Includes a summary of all calibration, maintenance, and repairs carried out on any major structure, equipment, apparatus, mechanism, or thing forming part of the Municipal Sewage Collection System.
- Includes a summary of any complaints related to the Sewage Works received during the reporting period and any steps taken to address the complaints.
- Includes a summary of all Alterations to the Authorized System within the reporting period including a list of Alterations that pose a Significant Drinking Water Threat.
- Includes a summary of all Collection System Overflow(s) and Spill(s) of Sewage, including:

- a) Dates;
- b) Volumes and durations;
- c) If applicable, loadings for total suspended solids, BOD, total phosphorus, and total Kjeldahl nitrogen, and sampling results for E.Coli;
- d) Disinfection, if any; and
- e) Any adverse impact(s) and any corrective actions, if applicable.

Includes a summary of efforts made to reduce Collection System Overflows, Spills, STP Overflows, and/or STP Bypasses, including the following items, as applicable:

- a) A description of projects undertaken and completed in the Authorized System that result in overall overflow reduction or elimination including expenditures and proposed projects to eliminate overflows with an estimated budget forecast for the year following that for which the report is submitted.
- b) Details of the establishment and maintenance of a PPCP, including a summary of project progress compared to the PPCP's timelines.
- c) An assessment of the effectiveness of each action taken.
- d) An assessment of the ability to meet Procedure F-5-1 or Procedure F-5-5 objectives (as applicable) and if able to meet the objectives, an overview of the next steps and estimated timelines to meet the objectives.
- e) Public reporting approach including proactive efforts.

The Town of Midland Wastewater System is in a fit state of repair and follows industry best practices during the repair and maintenance of the system. Infrastructure review occurs regularly between Engineering and Wastewater Services to optimize priority projects and minimize common costs.

Copies of the Amended Environmental Compliance Approval *5708-A72SPG* as issued July 20th, 2016, and Consolidated Linear Infrastructure (CLI) for the Wastewater Collection System 122-W601 as issued August 15th, 2023. are available upon request.

Introduction

The Town of Midland has prepared this Performance Report for the operations conducted during the 2025 calendar year.

This Performance Report has been prepared to meet the following commitments:

- To provide the Town of Midland, as “the Owner” of the sewage works, a summary of the operation and maintenance of the wastewater treatment plant that took place during the reporting period of January 1st, 2025, to December 31st 2025, and
- To comply with Condition 11 of ECA #5708-A72SPG and Schedule E 4.6 of the CLI 122-W601

This Performance Report, provided to the Town of Midland Council, conveys information related to the performance of operations and maintenance, which aids in decision-making related to system upgrades and expansion needs.

Ministry of the Environment, Conservation and Parks

The Midland Wastewater Treatment Plant is a conventional activated sludge plant owned and operated by the Town of Midland. The wastewater treatment plant was originally constructed in 1965 as a primary treatment plant. In 1980 the plant was expanded and upgraded to a secondary treatment facility. The treated effluent is discharged via a gravity outfall into Midland Bay (located on Georgian Bay). Environmental Compliance Approval (ECA) Number 5708-A72SPG was issued on July 20th, 2016, and governs the operation of the facility. The ECA identifies an average day design capacity of 15,665 m³/day and a Peak Flow Rate of 37,000 m³/day.

The treatment plant and collection system are operated under the following Certificates of Classification:

Class III Wastewater Treatment Certificate #89
Class II Wastewater Collection Certificate #2074

For the reporting period covered in this report, The Corporation of the Town of Midland was defined as the Operating Authority of the Wastewater Treatment Plant and the associated Wastewater Collection System.

Midland Wastewater Treatment Plant 2025 Effluent Flows (m ³)												
DATE	January	February	March	April	May	June	July	August	September	October	November	December
Total	214,690.33	164,190.85	370,396.28	310,934.92	201,245.32	179,428.34	176,894.46	163,447.48	154,418.48	146,342.97	197,010.31	209,069.27
Avg.	6,925.49	5,863.96	11,948.27	10,364.50	6,491.78	5,980.94	5,706.27	5,272.50	5,147.28	4,720.74	6,567.01	6,744.17
Max.	10,774.18	7,066.50	25,443.97	24,483.08	9,149.97	7,599.30	7,011.54	6,994.67	6,173.75	8,097.87	9,130.20	11,088.09
Min.	5,924.98	5,127.90	5,507.40	7,214.02	5,687.56	5,193.04	5,036.91	4,562.33	4,073.02	44.15	5,500.90	5,663.70
Average Daily Flow	6,811.08											
Max Daily Flow	25,443.97											
YEARLY TOTAL	2,488,069.01											

Figure 1: Midland Wastewater Treatment Plant 2025 Effluent Flow

Flows

The 2025 average daily flow was 6,811.08 m³ or 40% of plant-rated capacity. The plant discharged a total of 2,488,069.01m³ for the reporting period of January 1st 2025 to December 31st, 2025. The 2025 maximum daily flow occurred on March 16th when the flow recorded was 25,443.97 m³. On this day Midland observed a large amount of precipitation and unusually mild temperatures.

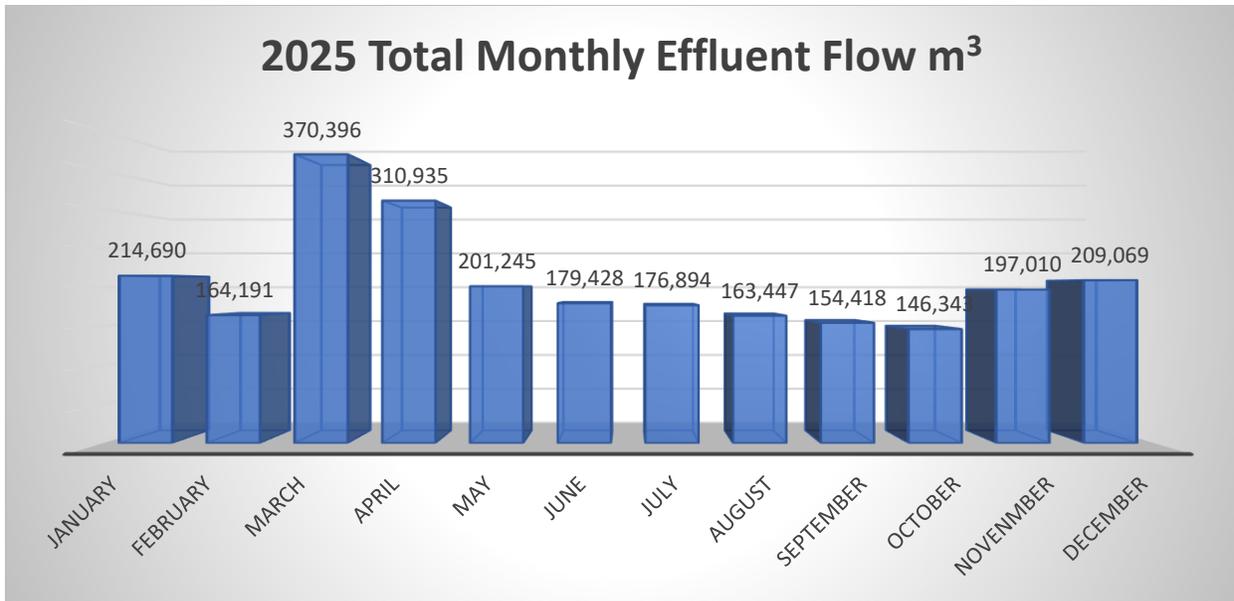


Figure 2: Monthly Effluent Flow in m³ for 2025.

Effluent Flow

The Total Monthly Discharge Flows are consistent throughout the year with an exception in March and April due to seasonal thaws and infiltration. Inflow and Infiltration (I&I) are continuously being evaluated in efforts to reduce the unnecessary treatment of rainwater and runoff during thaw seasons and storm events.

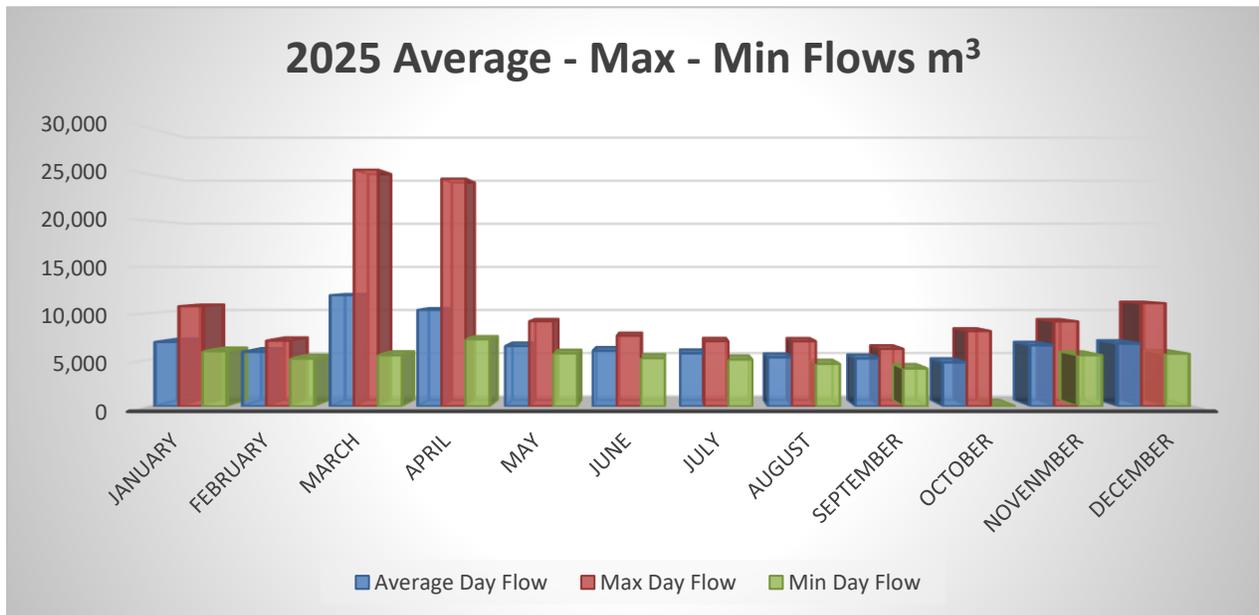


Figure 3: Monthly Average, Max and Min Day Flows in m³ for 2025.

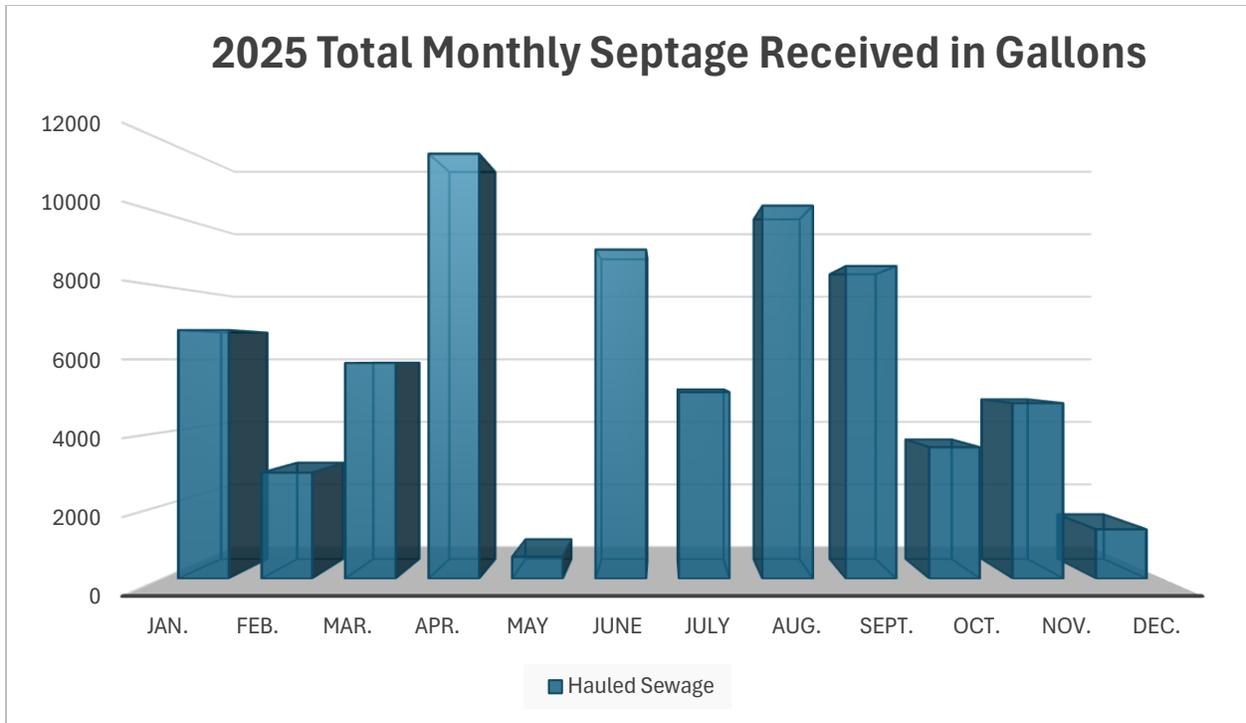


Figure 4: Total Monthly Septage Received m³ for 2025.

Septage Receiving

Within the reporting period of January 1st, 2025, to December 31st, 2025, the Wastewater Treatment Plant receives additional sewage in the forms of septic and holding tanks, portable toilets, grease traps, marine waste, and recreational vehicle holding tanks. The septage received is stored in holding tanks and pumped to the primary clarifier at a time so as not to upset the treatment process. **Currently, only septage from Midland’s municipal boundaries is being accepted.**

Influent and Effluent ECA Wastewater Parameters

Midland Wastewater Treatment Plant 2025 Effluent Loading				
Effluent Parameter	Effluent Objectives			
	Concentration Objective		Loading Objective	
	ECA Objective mg/l	Midland WTC Concentration mg/l	ECA Objective kg/Month	Midland WTC Loading kg/Month
CBOD⁵	7	3.00	4856	570.00
Total Suspended Solids	7	5.40	4856	1147.44
Total Phosphorus	0.3	0.114	146	21.94
Total Ammonia	5	2.80	1.69	
June 1st to August 31st			6.13	
Total Residual Chlorine	<0.02	0.006		
Effluent Limits				
Effluent Parameter	Average Concentration		Average Loading	
	ECA Limit mg/l	Midland WTC Concentration mg/l	ECA Limit kg/Year	Midland WTC Concentration kg/Year
CBOD⁵	10	3.00		
Total Suspended Solids	10	5.40		
Total Phosphorus				
Monthly Limit	0.4	0.114		
Annual Limit	0.5	0.114	1716	263.28
Total Ammonia				
June 1st to August 31st	10	6.13		
September 1st to May 31st	15	1.69		
Total Residual Chlorine	0.02	0.006		

Figure 5: Total Monthly Effluent Loading for 2025

Summary and Interpretation of Monitoring Data

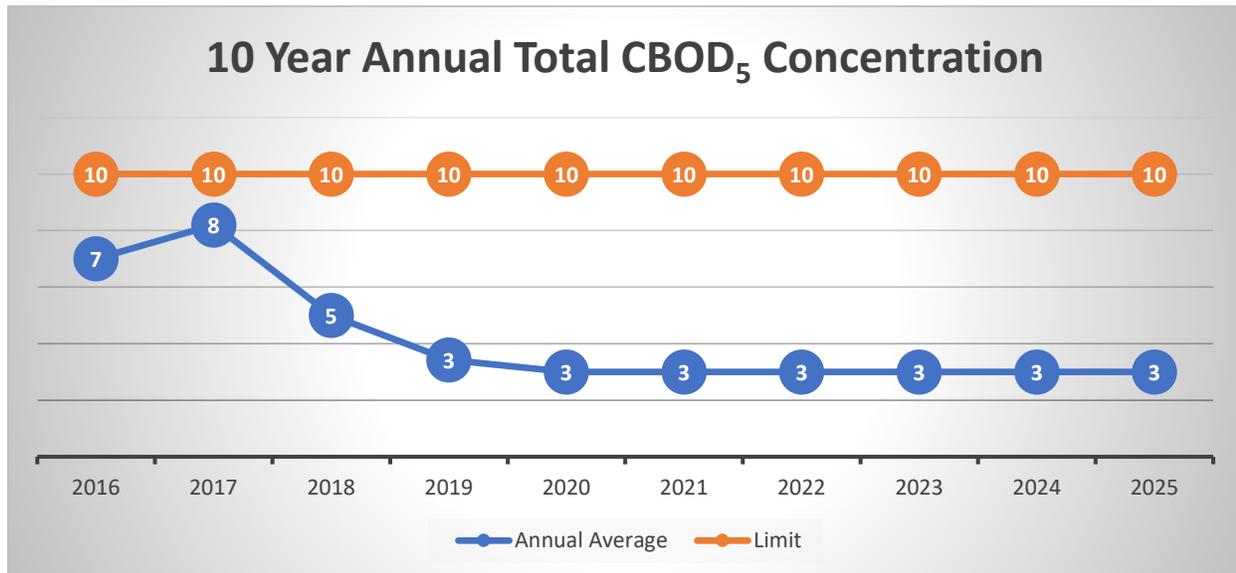


Figure 6: 10 Year Annual Total CBOD₅.

Total CBOD₅

From the ECA, the Annual Average Concentration limit for Carbonaceous Biochemical Oxygen Demand (CBOD₅) to the environment is 10 mg/l. During the Reporting Period of January 1st, 2025, to December 31st, 2025, Midland's Monthly Average CBOD₅ was 3.0 mg/l and the Annual Average was 3.0 mg/l. CBOD₅ is a 5-day test that represents the quantity of oxygen that is consumed during aerobic processes of decomposition of organic materials, caused by microorganisms.

The BOD therefore provides information on the impact the organic portion of the effluent will have on the oxygen level of the receiving stream, and on the aquatic life of the bay.

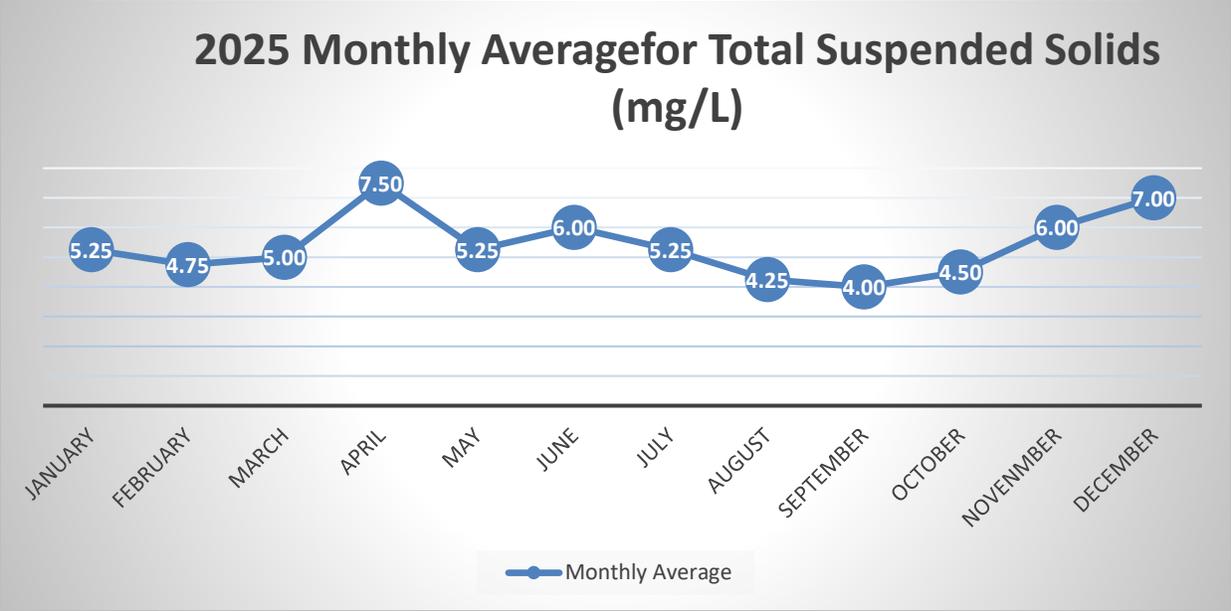


Figure 7: Monthly Average for Total Suspended Solids in mg/L.

Total Suspended Solids

As defined in the ECA, Annual Average Concentration limit for Total Suspended Solids (TSS) released to the environment is 10 mg/l. During the Reporting Period of January 1st, 2025, and December 31st, 2025, Midland’s Annual Average was 5.40 mg/l. TSS can include a wide variety of material, such as silt, decaying plant and animal matter, and industrial wastes. High concentrations of suspended solids can lower water quality by absorbing light. Waters then become warmer and lessen the ability of the water to hold oxygen necessary for aquatic life.

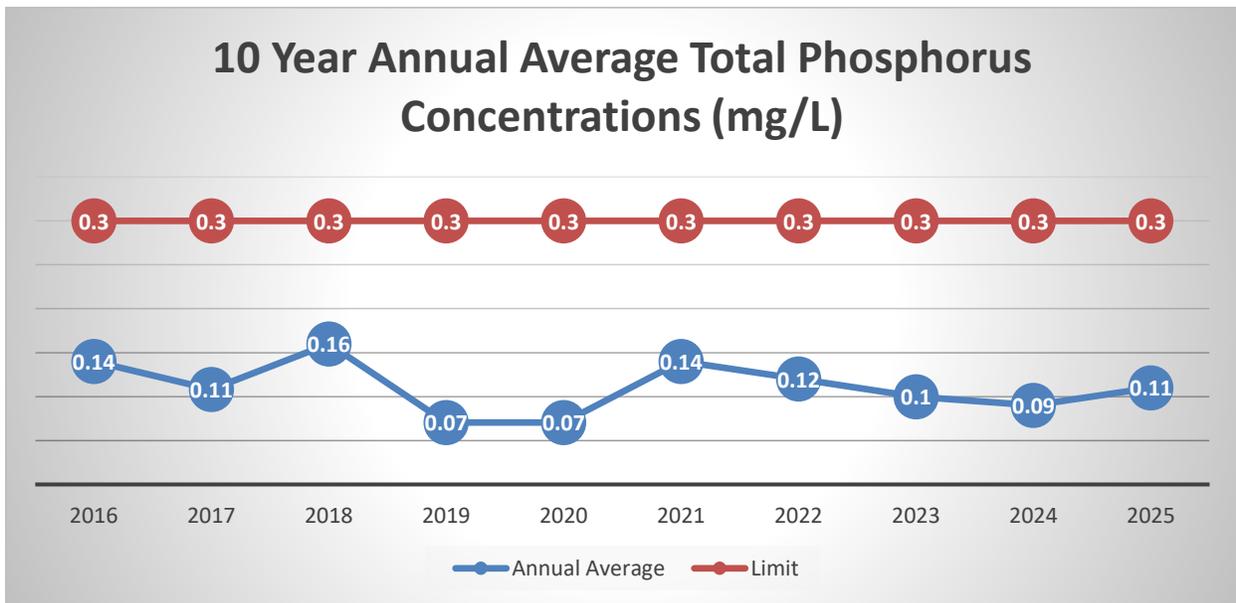


Figure 8: 10 Year Annual Average Total Phosphorus Concentrations

Total Phosphorus

Total Phosphorus is the sum of reactive, condensed and organic phosphorous. It is an essential element for plant life, but when there is too much of it in water, it can speed up eutrophication (a reduction in dissolved oxygen in water bodies caused by an increase of mineral and organic nutrients) of rivers and lakes.

The highest average monthly total phosphorus concentration of 0.17 mg/L took place during the month of August. This concentration results in a total monthly loading for August of 28.19 kg.

The annual average concentration of 0.114 mg/L was below the annual yearly objective of 0.3 mg/L and well below the 0.4 mg/L monthly limit dictated by the ECA. The total annual phosphorus loading of 263.28 kg/year is well below the ECA limit of 1,716 kg/year. The monthly objective for phosphorus of 146 kg/month was also achieved with a monthly loading average of 40.50 kg/ month

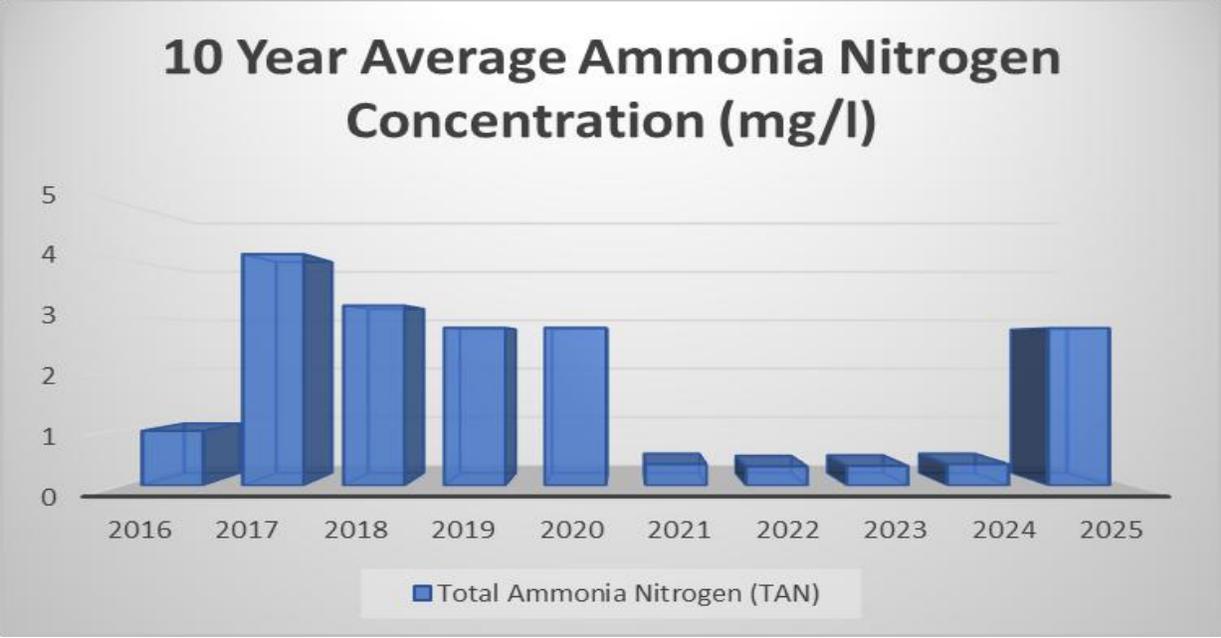


Figure 9: 10 Year Annual Average Total Ammonia Nitrogen Concentration

Total Ammonia Nitrogen

Total Ammonia is the sum of the free ammonia-nitrogen plus the amount of nitrogen from ammonia that has combined with chlorine. Ammonia pollution is a matter of increasing concern for regulatory authorities because of the serious threat it poses to the balance of sensitive habitats and to flora and fauna. Controlling ammonia discharges from wastewater treatment can make a significant contribution to reducing its environmental impact.

The average concentration of Total Ammonia Nitrogen (T.A.N.) between June 1st, 2025, to August 31st, 2025 (Summer) was 6.13 mg/L, the ECA limit is 10 mg/L.

The average concentration of Total Ammonia Nitrogen (T.A.N.) between January 1st, 2025, to May 31st, 2025 and September 1st, 2025 and December 31st 2025 (Winter) was 1.69 mg/L, the ECA limit is 15 mg/L.

The loading objective 5.0 mg/l identified in the ECA was also achieved for the reporting period of January 1st, 2025, to December 31st, 2025.

Midland Wastewater Treatment Plant 2025 Chlorine Usage and Effluent Residuals														
	January	February	March	April	May	June	July	August	September	October	November	December	Total	Monthly Average
Monthly Chlorine Usage	511.93	534.41	513.65	335.36	449.75	373.50	289.68	329.99	331.94	315.35	380.53	295.77	4661.86	
Monthly Average Daily Chlorine Use	16.51	19.09	16.57	11.18	14.51	12.45	9.34	10.64	11.06	10.17	12.68	9.54		12.81
Monthly Average Effluent Residual	0.003	0.009	0.014	0.008	0.012	0.004	0.004	0.007	0.008	0.013	0.008	0.025		0.010

Figure 10: Monthly and daily chlorine usage in Kg's.

Chlorine Usage

The monthly usage of Chlorine was consistent throughout 2025 with a total usage of 4661.86 kg. The average daily usage also remained consistent and remained between 9.34 kg/day and 119.09 kg/day for the reporting period of January 1st 2025 and December 31st, 2025. The Total Chlorine Residual of 0.010 mg/l in the Effluent was well below the 0.02 mg/l Objective and Limits set out in the ECA.

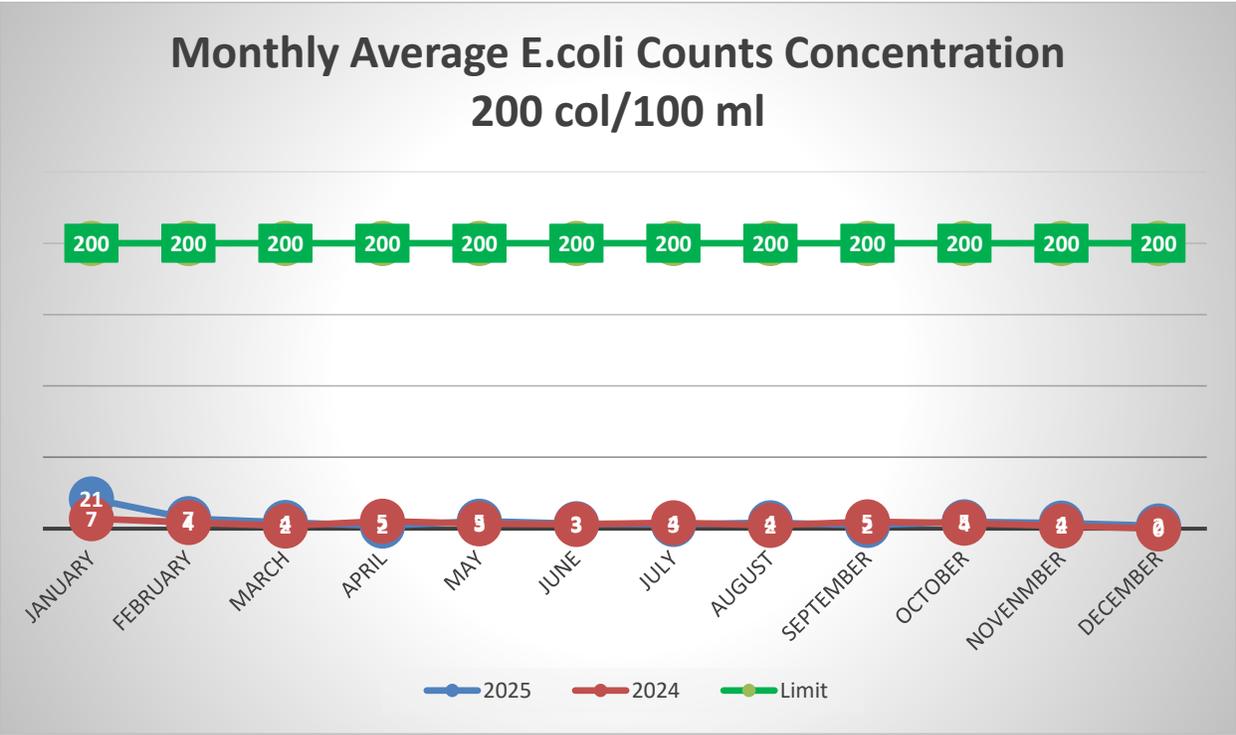


Figure 11: Monthly Average E.Coli Count Concentration 200 col/100 ml

E.Coli

Escherichia coli (*E. coli*) are a group of bacteria commonly found in the intestines of warm-blooded animals, including people. *E. coli* in freshwater can indicate the presence of pathogens (disease-causing organisms) from animal or human feces. The pathogens can cause illness for anyone who ingests them.


From the ECA, the E.Coli. on a Monthly Geometric Mean, must be less than 200 Colony-Forming units/100 ml (CFU's) released to the environment. Midland's 2025 Monthly Average E.coli count was 4 organisms per 100 ml .

Operational Improvements

Artificial Intelligence

To develop an efficient life-cycle management strategy for wastewater infrastructure assets, and maintain good levels of service, we are faced with the challenge of making decisions that not only prevent pipe failures whenever possible, but also minimize the consequences of these failures. Consequently, an effective risk management decision support system should integrate both likelihood and failure (LoF) and cost of failure (CoF) of linear assets to improve the overall reliability of the water and wastewater distribution networks. However, predicting each of these components accurately is a task that presents several challenges.

On the one hand, the likelihood of failure of a given pipe depends not only on its physical and structural characteristics, but also environmental and operational factors. Given the very high number of parameters that can reduce the useful life of linear infrastructure, a computational, AI-based approach can leverage existing sewer infrastructure and failure history data to identify groups of pipes that are most at risk of failure.

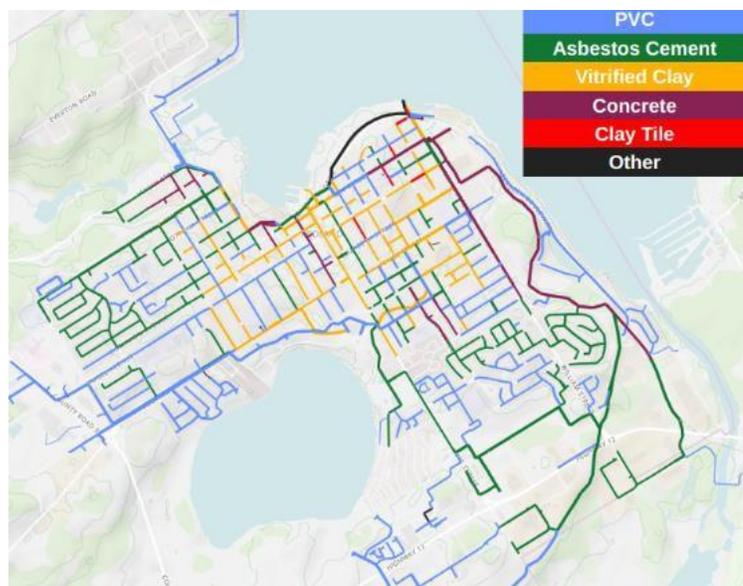

On the other hand, cost of failure estimation has traditionally been a highly subjective endeavor, which can be attributed to the fact that - direct and indirect - economic, social, and environmental costs are usually difficult to quantify and compare. However, by combining historical work order data and domain knowledge from municipal staff, it is possible to build a data-driven model that provides the most up-to-date insights regarding the potential socio-economic impacts of future pipe failures.

As such, these datasets are now being used in conjunction with Machine Learning algorithms to identify the most critical pipes in terms of overall risk, which combines their likelihood of failure as well as their cost of failure. The use of innovative, data-driven decision-making tools will help ensure that future investments have the greatest positive impact while limiting adverse consequences related to infrastructure failure.

NASM/Biosolids

In 2025, 12,620 m³ of Digested Biosolids were hauled from the Town of Midland Wastewater Treatment Plant under contract L04-49844 by Region of Huronia Environmental Services (ROHES). This is a 1% Increase from 2024. Efforts by staff to increase supernatant procedures has reduced the amount of Biosolids hauled by ROHES and stored at lagoons located in New Lowell during the winter months and apply to land in the summer months. Biosolids production volumes are expected to be near or slightly less in the 2026 calendar year.

2025 Biosolids Generated and Hauled

2025	January	February	March	April	May	June	July	August	September	October	November	December	Total
Loads	24	20	22	24	34	29	22	25	17	36	23	21	297
Volume m ³	1008	836	921	1009	1412	1218	924	1092	716	1499	1060	925	12620

Table 1: 2025 Biosolids Generated and Hauled

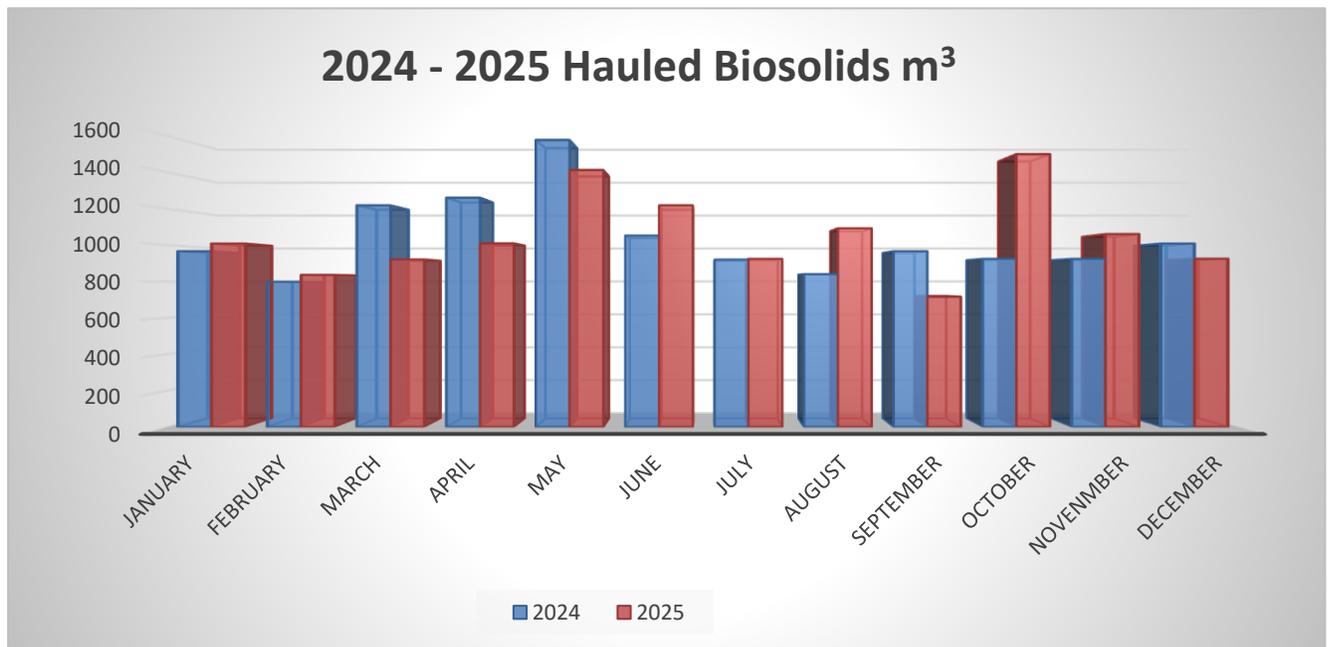


Figure 12: 2024-2025 Hauled Biosolids

Summary of Effluent Quality Assurance and Control Measures

Midland Wastewater Operators collect samples from Raw Sewage, Primary Clarifier Effluent, Aeration Effluent, Primary and Secondary Digesters, and Final Effluent regularly throughout the work week and month. Staff use standardized and accepted laboratory techniques when samples are tested for various parameters in-house for process control and effluent quality assurance. A spreadsheet is used to track in-house lab results to perform several calculations used to monitor and measure the effectiveness of the plant's performance. In addition to the in-house analysis, samples are collected weekly and sent to a certified laboratory, Caduceon Environmental Laboratories. These sample results are used to determine compliance with the ECA and Ministry Regulation.

Bypasses and Overflows

There were (2) By-pass events during the reporting period of January 1st 2025 to December 31st 2025. The measured volume receiving primary treatment to the outfall to Georgian Bay was 2592 m³.

Overflows are reported to the Ministry of Environment, Conservation and Parks (MECP) as well as to the Town of Midland's social platforms.

2025 By-Pass and Overflow Report					
Date	Location	Type	Volume m ³	Duration (Hrs)	Rainfall (mm)
March 16, 2025	Plant	By-pass	2000	8.5	N/A
April 03, 2025	Plant	By-pass	592	8.5	N/A

Applicable reports are found in Appendix A of this report.

Calibrations

All flow meters, level transmitter, probes and analyzers are calibrated as per the manufacturer's recommendations by a trained, knowledgeable and experienced technician. Calibrations are completed a minimum of once a year. Calibration was completed in June 2025 by SCG Flowmetrix. Calibration Certificates are submitted and retained electronically for each unit and devices. Below is a list of locations of units and devices and description.

	Date	Location	Description	Serial #
1	June 16 2025	Midland WWTP	WAS Flow Meter	A98 14063
2	June 16 2025	Midland WWTP	RAS Flow Meter	302418
3	June 16 2025	Midland WWTP	Final Effluent Flow Meter	PBD/L3050094
4	June 16 2025	Midland WWTP	Raw Sewage Tank Level	PDB/K0020132
5	June 19 2025	Midland WWTP	Bypass Chamber B Sanitary	N/A
6	June 19 2025	Midland WWTP	Bypass Chamber B Storm	N/A
7	June 16 2025	Midland WWTP	Calcium Thiosulfate Level North	PBD/A6281118
8	June 16 2025	Midland WWTP	Calcium Thiosulfate Level South	PBD/A680892
9	June 16 2025	Midland WWTP	Dechlor Chemical Flow Meter	N1K1225102
10	June 16 2025	Midland WWTP	Storm Tank Overflow Meter	PBD/L3271235
11	June 17 2025	Midland WWTP	Storm Tank Level	PBD/L3271195
12	June 17 2025	Midland WWTP	Influent Flow Meter	N/A
13	June 16 2025	Midland WWTP	Primary Raw Sludge Flow Meter	A964188
14	June 16 2025	Midland WWTP	Alum Pump #1 Flow Meter	N1K2145086
15	June 16 2025	Midland WWTP	Alum Pump #2 Flow Meter	N1K2145145
16	June 16 2025	Midland WWTP	Bio-Solids Haulage Flow	N1K502510
17	June 16 2025	Midland WWTP	Septage Tank Level	N/A
18	June 17 2025	Midland WWTP	Chlorine Tank Level	JNB/M8200000024
19	June 16 2025	Midland WWTP	Secondary Flow to Clarifier	N/A
20	June 16 2025	Midland WWTP	Sodium Hypochlorite Flow	N1K4105037
21	June 17 2025	Aberdeen SPS #3	Well Level	N/A
22	June 17 2025	Aberdeen SPS #3	Station Flow	PBD/L0234564
23	June 17 2025	Pillsbury SPS #4	Well Level	PBD/M3040016
24	June 17 2025	Pillsbury SPS #4	Station Flow	3K620000240145
25	June 18 2025	Howard SPS #5	Well Level	N/A
26	June 18 2025	Howard SPS #5	Station Flow Meter	N1LO105139
27	June 18 2025	Vindin SPS #6	Well Level	PBD/W2190022
28	June 16 2025	Vindin SPS #6	Outflow Meter	1320A359
29	June 18 2025	Bay Port SPS #7	Station Flow Meter	282948
30	June 18 2025	Bay Port SPS #7	Well Level	PBD/X5290260
31	June 16 2025	Chamber A Storm	Bypass Flow Meter	JNB/M7160000003
32	June 16 2025	Chamber A Storm	Bypass Flow Meter	JNB/M8070000005
33	June 19 2025	Bay SPS #1	Well Level	N/A
35	June 19 2025	Midland WWTP	Strainer Inlet Pressure	K8273700
34	June 19 2025	Midland WWTP	Strainer Outlet Pressure	K8273700

Summary of Maintenance Performed Throughout the Reporting Period

In addition to regular maintenance management programs and maintenance to all effluent monitoring equipment, works were upgraded or replaced by the Capital Plan as follows:

Treatment and Lift Station Facilities

- New Aeration System

Collection System

- SL-RAT Program
- Collection System Cleaning
- Lift Station Clean Outs
- Yonge St – Sanitary Relining
- Ellen St – Sanitary Replacement

Summary of Complaints Received Throughout the Reporting Period

There were no complaints received by the Town of Midland municipal staff throughout the Reporting Period for the Town of Midland Wastewater Treatment Plant for odour.

Summary of monitoring data

The collection system's current operational status is satisfactory, with no data indicating a need for immediate changes. Ongoing vigilance and routine checks are recommended to maintain this level of performance and to make informed decisions about any necessary adjustments in response to evolving conditions or demands.

Summary of efforts made to reduce Collection System Overflows

Efforts to reduce Collection System Overflows (CSOs) encompass a comprehensive approach aimed at enhancing the reliability and efficiency of sewer systems. These efforts include:

- Sewer Relining: This involves the application of a new liner inside existing sewer pipes to seal cracks, prevent leaks, and improve flow capacity without the need for extensive excavation. Sewer relining extends the life of sewer infrastructure and is a cost-effective method to mitigate overflows.
- Sewer Repair: Repair work is essential for addressing immediate issues such as blockages, breaks, and collapses in the sewer system. Timely repairs prevent minor issues from escalating into major overflows, thus maintaining the system's integrity.
- Inspection: Regular inspections are crucial for identifying potential problems before they lead to overflows. Inspections help in detecting cracks, blockages, root intrusions, and other issues that might compromise the sewer system's functionality.

- **CCTV Work:** Closed-circuit television (CCTV) inspections provide a detailed view of the sewer system's internal conditions. This technology enables the identification of defects and obstructions within pipes, facilitating targeted repairs and maintenance.
- **Acoustic Assessments:** Acoustic monitoring techniques are used to detect changes in the flow characteristics within the sewer system. These assessments can identify potential blockages or abnormalities in the system, often before they become visible or lead to overflows.
- **Installation of Monitoring Equipment:** Advanced monitoring equipment, such as flow meters and level sensors, are installed within the sewer system to provide real-time data on flow rates and levels. This information is crucial for early detection of overflow conditions and for making informed decisions on system operations.
- **Strategic Asset Replacements:** Aging or severely damaged sections of the sewer system are strategically replaced to ensure reliability and to prevent overflows. This involves prioritizing replacements based on risk assessments and the critical nature of the assets to the overall system performance.

These efforts collectively contribute to reducing the incidence and impact of Collection System Overflows by enhancing the structural integrity, capacity, and operational efficiency of sewer systems. Through a combination of technological advancements, strategic planning, and proactive maintenance, municipalities and utility companies can effectively manage and mitigate the challenges associated with CSOs.

Details of Procedure F-5-5 are being met, and all reasonable efforts to reduce CSOs will continue.

Additional Sampling

The Federal Government for the Department of Oceans and Fisheries require the WWTP to sample for Acute Lethality Testing. An acute lethality test with fish for wastewater involves exposing selected fish species to wastewater samples under controlled conditions to assess toxicity. The test, usually lasting 96 hours, monitors fish survival and health at various wastewater concentrations. Results help gauge the wastewater's impact on aquatic life. The results are included in Appendix B of this report.

Limited Operational Flexibility-Notice of Modifications Form

There were no Limited Operation Flexibility or Notice of Modification forms submitted throughout the Reporting Period. All upgrades/modifications have been completed following the Terms and Conditions of the ECA.

Closing Remarks

Throughout the Reporting Period the Midland WWTP and Collection System have been operated to the best of its ability while subject to construction activity, and seasonal influences. With continued construction and typical average daily flows, operations staff expect the WWTP to operate as designed over the next Reporting Period.

APPENDIX A



Emergency Overflow Report

Chamber "A" or "B"	Chamber A <input type="checkbox"/> Chamber B <input checked="" type="checkbox"/>
Bypass Start Date:	16/03/2025
Bypass Start Time:	15:00:00
Bypass Stop Date:	16/03/2025
Bypass Duration (min):	8 hrs 30 minutes
Total Bypass Flow (m3):	2000 m3

C.O.C.: -

REPORT No: 25-006565 - Rev. 0

Report To:
 Town of Midland
 575 Dominion Ave.
 Midland, ON L4R 1R2

CADUCEON Environmental Laboratories
 112 Commerce Park Dr Unit L
 Barrie, ON L4N 8W8

Attention: Andre Pepin

DATE RECEIVED: 2025-Mar-17
 DATE REPORTED: 2025-Mar-25
 SAMPLE MATRIX: Waste Water

CUSTOMER PROJECT: Storm Tank Bypass
 P.O. NUMBER:

Analyses	Qty	Site Analyzed	Authorized	Date Analyzed	Lab Method	Reference Method
CBOD5 (Liquid)	4	KINGSTON	DCASSIDY	2025-Mar-19	BOD-001	SM 5210B
Cond/pH/Alk Auto (Liquid)	4	OTTAWA	SBOUDREAU	2025-Mar-18	COND-02/PH-02/A LK-02	SM 2510B/4500H/ 2320B
E.Coli m-TECH Media (Liquid)	4	BARRIE	IMANOJ	2025-Mar-17	EC-001	MECP E3371
Ammonia (Liquid)	4	KINGSTON	DCASSIDY	2025-Mar-18	NH3-001	SM 4500NH3
TP & TKN (Liquid)	4	KINGSTON	YLIEN	2025-Mar-20	TPTKN-001	MECP E3516.2
TSS (Liquid)	4	KINGSTON	MCLOSS	2025-Mar-19	TSS-001	SM 2540D

R.L. = Reporting Limit
 NC = Not Calculated


Test methods may be modified from specified reference method unless indicated by an *

Parameter	Units	R.L.	Client I.D.			
			Storm Tank Bypass A	Storm Tank Bypass B	Storm Tank Bypass C	Storm Tank Bypass D
			Sample I.D.	Sample I.D.	Sample I.D.	Sample I.D.
			25-006565-1	25-006565-2	25-006565-3	25-006565-4
			Date Collected	Date Collected	Date Collected	Date Collected
			2025-03-16	2025-03-16	2025-03-16	2025-03-16
			-	-	-	-
E coli	CFU/100mL	1	72000	800	1500	600
pH @25°C	pH units	-	7.76	7.89	7.91	7.74
CBOD5	mg/L	3	12	19	18	9
Total Suspended Solids	mg/L	3	40	28	25	36
Phosphorus (Total)	mg/L	0.01	0.99	0.89	0.87	0.74
Ammonia (N)-Total (NH3+NH4)	mg/L	0.05	3.38	2.84	2.83	2.67
pH (Client Data)	pH units	-	7.82	7.48	7.56	7.37
Temperature (Client Data)	°C	-	7.8	10	9.1	6.7



Michelle Dubien
 Data Specialist

The analytical results reported herein refer to the samples as received and relate only to the items tested. Reproduction of this analytical report in full or in part is prohibited without prior consent from Caduceon Environmental Laboratories.



Emergency Overflow Report

Chamber "A" or "B" or Storm Tank	Chamber A <input type="checkbox"/> Chamber B <input type="checkbox"/> Storm Tank <input checked="" type="checkbox"/>
Bypass Start Date:	03/04/2025
Bypass Start Time:	03:28 AM
Bypass Stop Date:	03/04/2025
Bypass Duration (min):	12:10 PM
Total Bypass Flow (m3):	592 m3

Midland Wastewater Quarterly ByPass/Overflow Report

Site Location: **Midland Sewage Treatment Plant**
 200 Bay Street
 Town of Midland, County of Simcoe, Ontario

Environmental Compliance Approval: **# 5708-A72SPG**
Issue Date: **July 20, 2016**

BY-PASSES

(3) The Owner shall submit By-pass and Plant Overflow Event Reports to the Ministry's local office on a **quarterly basis**, no later than each of the following dates for each calendar year: February 14, May 15, August 14, and November 15. Event Reports shall be in an electronic format specified by the Ministry. In each Event Report the Owner shall include, at a minimum, the following information on any Events that occurred during the preceding quarter:

- (a) the date of the Event(s);
- (b) the measured or estimated volume of the Event(s);
- (c) the duration of the Event(s);
- (d) the location of the Event(s);
- (e) the reason for the Event(s); and
- (f) the level of treatment the By-pass(es) and/or Plant Overflow(s) received and disinfection status of same.

Please consider this as our Quarterly By-Pass/Overflow Report for:

a) Date: **January 01, 2025 to March 31, 2025**

b) Volume:

 By-Pass m³: **2000.0**

 Overflow m³: **0.0**

There were no By-Passes or Overflows for Q1

c) Duration: 8.50

d) Location: Storm Tank

e) Reason/Event: Weather Event

f) Treatment: Chlorine

Midland Wastewater Quarterly By-Pass/Overflow Report

Site Location: **Midland Sewage Treatment Plant**
 200 Bay Street
 Town of Midland, County of Simcoe, Ontario

Environmental Compliance Approval: **# 5708-A72SPG**

Issue Date: **July 20, 2016**

BY-PASSES

(3) The Owner shall submit By-pass and Plant Overflow Event Reports to the Ministry's local office on a **quarterly basis**, no later than each of the following dates for each calendar year: February 14, May 15, August 14, and November 15. Event Reports shall be in an electronic format specified by the Ministry. In each Event Report the Owner shall include, at a minimum, the following information on any Events that occurred during the preceding quarter:

- (a) the date of the Event(s);
- (b) the measured or estimated volume of the Event(s);
- (c) the duration of the Event(s);
- (d) the location of the Event(s);
- (e) the reason for the Event(s); and
- (f) the level of treatment the By-pass(es) and/or Plant Overflow(s) received and disinfection status of same.

Please consider this as our Quarterly By-Pass/Overflow Report for:

a) Date: **April 01, 2025 to June 30, 2025**

b) Volume:

By-Pass m³: **592.0**

Overflow m³: **0.0**

There were no By-Passes or Overflows for Q2

c) Duration: 8:42

d) Location: Storm Tank

e) Reason/Event: Weather Event

f) Treatment: Chlorine

APPENDIX B



TOXICITY TEST REPORT
Rainbow Trout
EPS 1/RM/13
Page 1 of 2

SAMPLE IDENTIFICATION

Sample Number :	PE2425-0083	Sampling Date :	2025-03-17
Company :	Town of Midland	Sampling Time :	19:30
Location :	Midland, ON	Date Received :	2025-03-19
Substance :	Final Effluent	Time Received :	12:10
Sampling Method :	Grab	Temperature at Receipt :	17.8°C
Sampled By :	J.B	Date Tested :	2025-03-20
Sample Description :	Clear light green		

96-HOUR TEST RESULTS

Substance	Effect	Value
Control	Mean Impairment	0.0 %
	Mean Mortality	0.0 %
100%	Mean Impairment	0.0 %
	Mean Mortality	0.0 %

The results reported relate only to the sample tested and as received.

TEST ORGANISM

Test Organism :	<i>Oncorhynchus</i>	Mean Fork Length :	37.0 mm
Organism Batch :	<i>mykiss</i>	Range of Fork Lengths :	32 - 42
Control Sample Size :	CC250115	Mean Wet Weight :	mm
Cumulative stock tank mortality rate :	10	Organism Loading Rate	0.5 g
	0% (previous 7 days)		

TEST CONDITIONS

Test Type :	Single	Number of Replicates :	1
Sample pH Adjustment :	Concentration	Organisms Per Replicate	10
Sample Pre-aeration/Aeration Rate :	No	:	10
Duration of Sample Pre-Aeration :	6.5 ± 0.26 mL/min/L	Organisms Per Test	20 L
:	30 minutes	Level :	20 L
Control Pre-aeration/Aeration Rate :	6.5 ± 0.26 mL/min/L	Volume of Sample :	None
:	30 minutes	Volume of Control :	

REFERENCE TOXICANT DATA

Toxicant :	Zinc	LC50 :	0.37 mg/L
Organism Batch :	CC250115	95% Confidence Limits	0.30 mg/L, 0.45 mg/L
Date Tested :	2025-03-10	:	mg/L
Statistical Method	Untrimmed Spearman-	Historical Mean LC50 :	0.38 mg/L

COMMENTS

SAMPLE IDENTIFICATION

Sample Number :	PE2425-0381	Sampling Date :	2025-06-20
Company :	Town of Midland	Sampling Time :	9:00
Location :	Midland, ON	Date Received :	2025-06-23
Substance :	Final Effluent	Time Received :	13:00
Sampling Method :	Grab	Temperature at Receipt :	29°C
Sampled By :	J.B.	Date Tested :	2025-06-24
Sample Description :	Clear, light green		

96-HOUR TEST RESULTS

Substance	Effect	Value
Control	Mean Impairment	0.0 %
	Mean Mortality	0.0 %
100%	Mean Impairment	0.0 %
	Mean Mortality	0.0 %

The results reported relate only to the sample tested and as received.

TEST ORGANISM

Test Organism :	<i>Oncorhynchus mykiss</i>	Mean Fork Length :	44.3 mm
Organism Batch :	LF250508-1	Range of Fork Lengths :	39 - 49
Control Sample Size :	10	Mean Wet Weight :	mm
Cumulative stock tank mortality rate :	0% (previous 7 days) 0% (at test)	Organism Loading Rate	0.8 g

TEST CONDITIONS

Test Type :	Single	Number of Replicates :	1
Sample pH Adjustment :	Concentration	Organisms Per Replicate	10
Sample Pre-aeration/Aeration Rate :	No		10
Rate :	6.5 ± 0.26 mL/min/L	Organisms Per Test	30 L
Duration of Sample Pre-Aeration :	30 minutes	Level :	30 L
Control Pre-aeration/Aeration Rate :	6.5 ± 0.26 mL/min/L	Volume of Sample :	None
		Volume of Control :	

REFERENCE TOXICANT DATA

Toxicant :	Zinc	LC50 :	0.32 mg/L
Organism Batch :	LF250508	95% Confidence Limits :	0.25 mg/L, 0.42 mg/L
Date Tested :	2025-06-04	Historical Mean LC50 :	mg/L
Statistical Method	UnTrimmed Spearman-	Warning Limits (± 2SD)	0.38 mg/L

COMMENTS



Suite 122, 704 Mara Street
 Point Edward, ON
 N7V 1X4
 Tel. (519) 339-8787

TOXICITY TEST REPORT

Rainbow Trout

EPS 1/RM/13

Page 1 of 2

SAMPLE IDENTIFICATION

Sample Number :	PE2526-0053	Sampling Date :	2025-09-17
Company :	Town of Midland	Sampling Time :	13:00
Location :	Midland, ON	Date Received :	2025-09-19
Substance :	Final Effluent	Time Received :	12:30
Sampling Method :	Grab	Temperature at Receipt (°C) :	23.1
Sampled By :	Not Provided	Date Tested :	2025-09-22
Sample Description :	Clear, light green		

96-HOUR TEST RESULTS

Substance	Effect	Value
Control	Mean Impairment	0.0 %
	Mean Mortality	0.0 %
100%	Mean Impairment	0.0 %
	Mean Mortality	0.0 %

The results reported relate only to the sample tested and as received.

TEST ORGANISM

Test Organism :	<i>Oncorhynchus mykiss</i>	Mean Fork Length :	47.9 mm
Organism Batch :	LF250710B	Range of Fork Lengths :	44 - 52 mm
Control Sample Size :	10	Mean Wet Weight :	mm
Cumulative stock tank mortality rate :	0% (previous 7 days) 0% (at test)	Organism Loading Rate	1.0 g

TEST CONDITIONS

Test Type :	Single	Number of Replicates :	1
Sample pH Adjustment :	Concentration	Organisms Per Replicate	10
Sample Pre-aeration/Aeration Rate :	No		10
Duration of Sample Pre-Aeration :	6.5 ± 0.26 mL/min/L	Organisms Per Test Level :	30 L
Control Pre-aeration/Aeration Rate :	30 minutes	Volume of Sample :	30 L
	6.5 ± 0.26 mL/min/L	Volume of Control :	None

REFERENCE TOXICANT DATA

Toxicant :	Zinc Sulfate Heptahydrate	LC50 :	0.22 mg/L
Organism Batch :	LF250710B	95% Confidence Limits :	0.17 mg/L, 0.28 mg/L
Date Tested :	2025-09-05	Historical Mean LC50 :	mg/L
Statistical Method	UnTrimmed Spearman-	Warning Limits (± 2SD)	0.38 mg/L

COMMENTS

SAMPLE IDENTIFICATION

Sample Number :	PE2526-0256	Sampling Date :	2025-12-02
Company :	Town of Midland	Sampling Time :	14:00
Location :	Midland, ON	Date Received :	2025-12-04
Substance :	Final Effluent	Time Received :	13:00
Sampling Method :	Grab	Temperature at Receipt	8.9
Sampled By :	Not Provided	(°C) :	2025-12-05
Sample Description	Clear, light		

96-HOUR TEST RESULTS

Substance	Effect	Value
Control	Mean Impairment	0.0 %
	Mean Mortality	0.0 %
100%	Mean Impairment	0.0 %
	Mean Mortality	0.0 %

The results reported relate only to the sample tested and as received.

TEST ORGANISM

Test Organism :	<i>Oncorhynchus mykiss</i>	Mean Fork Length :	49.5 mm
Organism Batch :	LF250926B	Range of Fork Lengths :	45 - 55
Control Sample Size :	10	Mean Wet Weight :	mm
Cumulative stock tank mortality rate :	0% (previous 7 days) 0% (at test)	Organism Loading Rate	1.2 g

TEST CONDITIONS

Test Type :	Single	Number of Replicates :	1
Sample pH Adjustment :	Concentration	Organisms Per Replicate	10
Sample Pre-aeration/Aeration Rate :	No		10
Duration of Sample Pre-Aeration :	6.5 ± 0.26 mL/min/L	Organisms Per Test	32 L
Control Pre-aeration/Aeration Rate :	30 minutes	Level :	35 L
	6.5 ± 0.26 mL/min/L	Volume of Sample :	None
		Volume of Control :	

REFERENCE TOXICANT DATA

Toxicant :	Zinc (as Zinc Sulphate)	LC50 :	0.37 mg/L
Organism Batch :	LF250926B	95% Confidence Limits :	0.27 - 0.51
Date Tested :	2025-12-01	Historical Mean LC50 :	mg/L
Analyst(s) :	SO, KK, KF	Warning Limits (± 2SD)	0.31 mg/L
Statistical Method	Linear Regression		

COMMENTS

